



**Highlight Photo – HS Phase I**  
**Elevated Track at Gym**  
**Looking to the South**

- The flooring contractor has installed the synthetic surface on the walking/track around the Gym. The bleachers are installed along with all of the other Gym equipment and the space is ready for the games to start.

The construction pace was extremely hectic at the end of the summer, but all three projects were ready for the opening of school as scheduled. The kitchen/cafeteria/media center portion of the project will be enclosed by the first part of October. The construction progress on the Auditorium is also back on track with the school back in session.

## Views from the Site

### **Progress Photo – HS Phase II** **Main Entrance** **Looking to the South**

- This photo was taken just before school resumed. There will be some miscellaneous items to complete, but all the work required to open school was completed as scheduled.



### **Progress Photo – HS Phase II** **Revised High School Office** **Looking to the Northeast**

- The Office Area was re-designed to incorporate a secured entrance and the whole layout of the Office was revised during the work this summer.



## Views from the Site

### **Progress Photo – HS Phase II** **Main North/South Corridor** **Looking to the North**

- This photo was taken in the new portion of the building at the south entrance, looking to the north. A vestibule was created at this entrance which will provide a service entrance to the new kitchen.



### **Progress Photo – HS Phase II** **New South Entrance** **Looking to the East**

- The majority of the work has been completed at the new south entrance. The metal panels and roof edge trim will be completed early this fall.



## Views from the Site

### **Progress Photo – HS Phase II** **Cafeteria Addition** **Looking to the West**

- The contractors are installing the exterior walls for the new Cafeteria/Kitchen building addition. There will be new large windows into the Cafeteria looking out onto Birch Street. The roof will be installed at this portion of the building in early fall.



### **Progress Photo – HS Phase II** **New Main Entrance** **Looking to the West**

- This is the new main entrance to the High School. The metal roofing and fascia panels will be installed in the near future. The opening on the left side of the photo will be a new window into the relocated Media Center.



## Views from the Site

### **Progress Photo – HS Phase I** **New Media Center** **Looking to the South**

- This is a view from the exterior of the building looking into the new Media Center. The center section of the floor is the old low seating area for the existing performance room. This has been filled in with sand and a new concrete slab will soon be installed to create a level floor surface.



### **Progress Photo – Site Work** **Main Commons Entrance** **Looking to the Southeast**

- The metal panels and aluminum doors have been installed at the new main entrance to the Gym and future Auditorium. The stockpile of block seen in the left side of the photo will be used for the interior walls of the Auditorium.



## Views from the Site

### **Progress Photo – HS Phase I** **Sports Deck Area** **Looking to the Southeast**

- This is the upper level in the southeast corner of the new Gym addition. The windows on the right are translucent panels that allow filtered, nature light to enter the space. The doors in the background lead to a large storage room that will be completed as part of the Phase II project.



### **Progress Photo – HS Phase I** **Weight Room** **Looking to the West**


- The school staff as move the weight training equipment into the new Weight Room and the space is ready to use. This is located on the upper level, south side of the Gym addition.



## Views from the Site

### **Progress Photo – HS Phase I** **Commons Area at Gym Addition** **Looking to the South**

- The new Commons Area has been completed and the space is ready to use. The Concession Area is located on the left and the large display cases and toilet rooms are on the right side. The space can be viewed from the upper level on three sides.

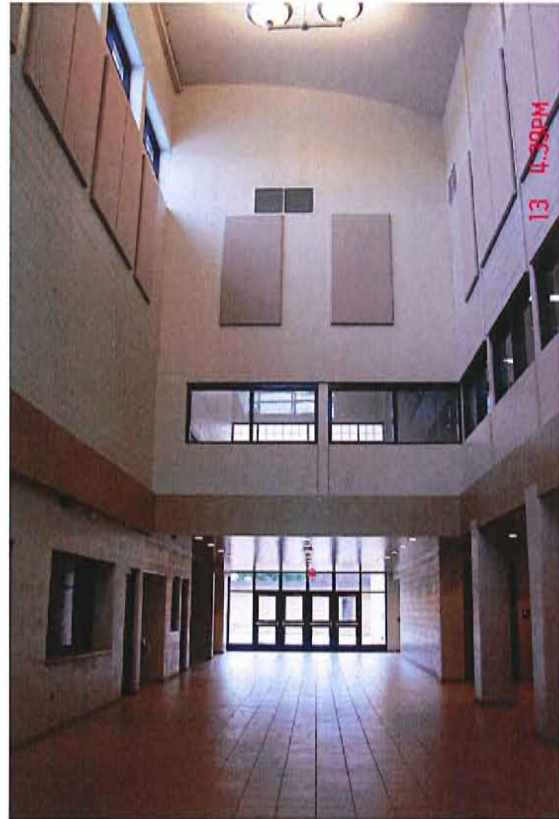

### **Progress Photo – MS Phase II** **Middle School Addition** **Looking to the North**

- The entrance addition at the Middle School has been completed. This will provide a vestibule and new toilets for the Gym Area.



## Views from the Site

### **Progress Photo – MS Phase II** **Addition at Middle School** **Looking to the North**

- The work is done and the space is ready to use. There are new display cases on the right side and the new toilet rooms are located on the left side. The floor surface was removed at the existing portion of the space and new flooring was installed throughout the existing area into the addition.



### **Progress Photo – MS Phase II** **New Toilet Rooms** **Looking to the Southwest**


- This photo shows the new windows at the addition and the concrete benches at the windows. The entire space received a new ceiling and lighting system.



## Views from the Site

### **Progress Photo – Birch Street** **New Classroom Corridor** **Looking to the North**

- The work has been completed and ready for the students. The new corridors will create a more traditional layout for the classrooms and circulation space. The students will also have new lockers.

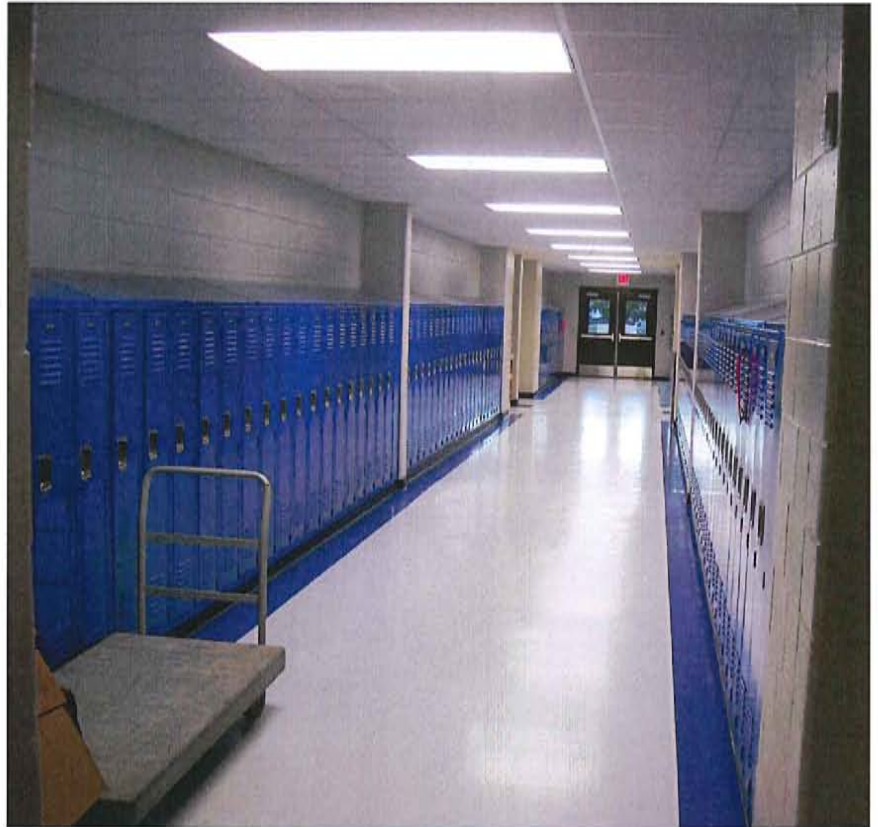

### **Progress Photo – Birch Street** **Revised Media Center** **Looking to the Northeast**

- The Media Center has been revised with new flooring, ceiling, lighting and new staff offices have been constructed within the space.



## Views from the Site

### **Progress Photo – Birch Street** **New Exterior Doors** **Looking to the West**

- With the addition of the new corridors, exterior egress doors were installed at the end of each corridor and new sidewalks were also installed at the doors.



### **Progress Photo – Birch Street** **Revised Main Office Entrance** **Looking to the Northwest**

- The main entrance at the Office was revised to incorporate a secured vestibule, similar to the one created at the High School. New casework, flooring, ceiling and lighting was also installed.



## Upcoming Construction Activities

### **High School – Phase I**

- Complete punch list work items

### **High School – Phase II**

- Complete masonry work at Cafeteria/Kitchen addition
- Complete steel work at Cafeteria/Kitchen addition
- Begin roofing at Cafeteria/Kitchen addition
- Complete interior masonry walls at Auditorium

### **Middle School – Phase II**

- Complete boiler replacement work
- Complete punch list work items

### **Birch Street Elementary School**

- Complete punch list work items
